

Bi-weekly Update

March 23, 2022

Progress to date:

As the 2022 construction season has kicked off, the following has been accomplished (February 21-March 22, 2022):

- Traffic control has been implemented to allow for utility work and bridge demolition efforts
- The east side of the LaCrosse Street bridge deck has been removed to prepare for construction of a parallel structure
- Utility work to replace water and sewer lines has been initiated south of the LaCrosse Street bridge

Two-week look-ahead


- Bridge berms will be shaped / constructed
- Retaining wall will be built adjacent to Burger King Property
- Cranes will be mobilized to start driving pile for the the new LaCrosse Street parallel structure
- Utility crews will move to the north side of the LaCrosse Street bridge. This phase is expected to last approximately four weeks



**Diverging Diamond
Interchange**



Equipment for Utility Replacement

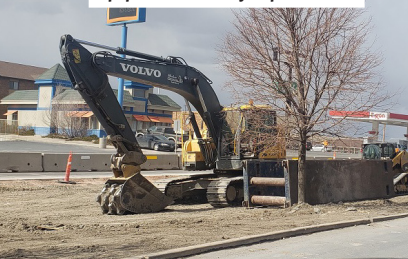

Retaining Wall Construction



Temporary Traffic Control



Follow the project progress on social media and
<https://www.i90lacrosseddi.com/construction.html>

