

Bi-weekly Update

Wednesday, April 20, 2022


Progress to date:

As the 2022 construction season ramps up, the following construction items have been accomplished during the timeframe of April 6 - April 19, 2022.

- The south bridge berm has been substantially completed.
- Storm sewer, south of the bridge, has been installed.
- The retaining wall on the northeast side of the bridge has been completed.

Two-week look-ahead:

- The retaining wall on the southeast side of the bridge will be constructed.
- The north bridge berm earthwork will be completed.
- City utility work will wrap up until August 2022 when the final tie-ins will be completed.
- Pre-bores and pile driving for north and south bridge supports will commence.
- Girder placement is planned to begin with nighttime Interstate closures at LaCrosse Street (Exit 59).

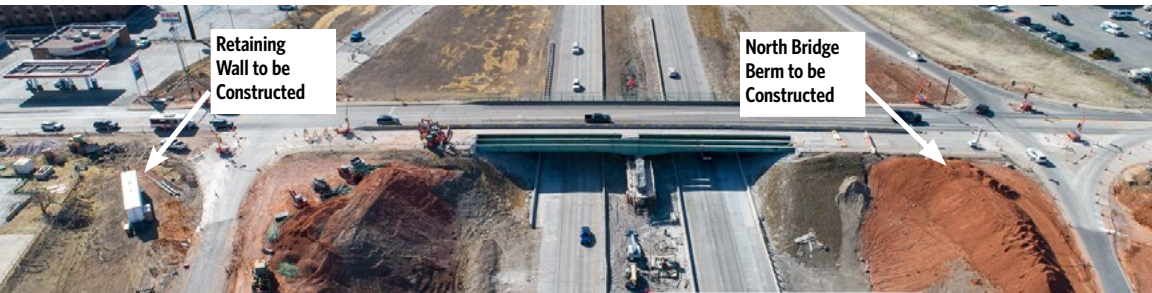

Retaining Wall to be Constructed

North Bridge Berm to be Constructed



Utility Replacement Construction is Nearing Substantial Completion



Preparing Center Pier Cap for Girder and Bearing Placement



Follow the project progress on social media and <https://www.i90lacrosseddi.com/construction.html>

