

# Bi-weekly Update

Thursday, June 16, 2022


## Progress to date:

As the 2022 construction season continues, the following construction activities have been accomplished during the time-frame of Wednesday, June 1 - Tuesday, June 14, 2022.

- Asphalt has been placed on LaCrosse Street, south of the bridge.
- The I-90 eastbound LaCrosse Street ramp was temporarily closed, effective Thursday, June 9, 2022, for 20 working days to build grade and pave the upper portion of the eastbound ramp.
- Sidewalk, additional curb and gutter, and partial ramp approaches have been placed.

## Two-week look-ahead:

- Crews will be setting forms for the north abutment wall and installing falsework for the new structure.
- Curb and gutter will be placed to form new islands and ramp edges.
- Additional asphalt will be placed in areas that have completed curb and gutter south and north of the bridge.
- Electrical conduit will be placed below grade for the new traffic signals, pedestrian signals, and street lights.

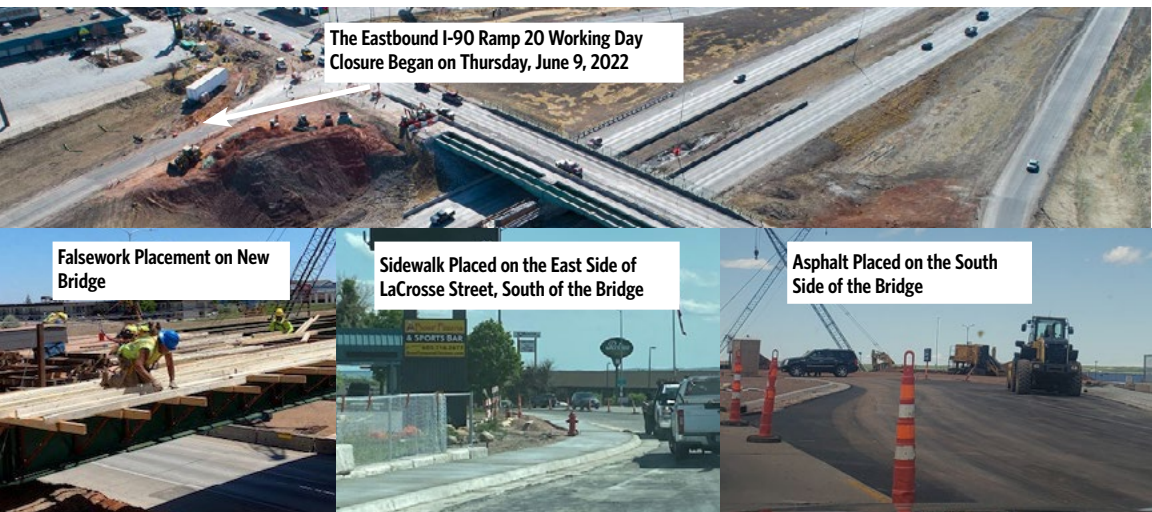

The Eastbound I-90 Ramp 20 Working Day Closure Began on Thursday, June 9, 2022

Falsework Placement on New Bridge

Sidewalk Placed on the East Side of LaCrosse Street, South of the Bridge

Asphalt Placed on the South Side of the Bridge

Follow the project progress on social media and <https://www.i90lacrosseddi.com/construction.html>

